ED ENGINEERING CON<u>SULTANTS, INC</u>

Building Condition Surveys
Contract Administration
Corrosion Control Design
Structural Inspection & Design
Project Planning & Management

FIELD OVSERVATION REPORT PERMIT # BLDC-000287-2020

		Report No. 74	Page 1 of 1
Project:	Southpoint Condominium	Inspection For:	Restoration Project
Day/Date:	Friday, January 15, 2021	Job No.	19-1086
Location:	4453 S. Atlantic Ave, Ponce Inlet	Engineer:	Timothy J. Snook, P.E.
Contractor:	ACE Enterprises, LLC	Project Foreman:	Wes Swaim
Subcontractor:	Gulfstream Glass (4)	Inspector:	Timothy J. Snook, P.E.
Weather:	48 Degrees @ 8:00 A.M. Sunny Light Breeze 0% Chance of Rain		
Workforce Total:	16		
Activities:	Concrete repair, stucco application, painting, window installation, coating removal		

Observation Report:


The Engineer was on-site to inspect completed concrete repairs on the divider walls in the garage, the header of Unit 406 window and on the walkways (See Photos 1-2). The excavations conformed to ICRI standards. The reinforcing steel was cleaned. The excavations were supplemented as directed. The excavations were approved to be cast. Forming and casting repairs is in-progress.

Stucco application is in-progress on the divider walls below the building.

Coating removal continues on the 02 and 03 stack balconies.

Paint application continues on the exterior perimeter walls of the pool deck.


Window installation is continues on the 6th floor of the 05 stack.



4240 South Ridgewood Avenue, Suite 4, Port Orange, FL 32127 • (386) 256-7684 • office@unitedengineeringconsultants.com Certificate of Authorization No. 6607



Picture 1: Unit 406 header repair

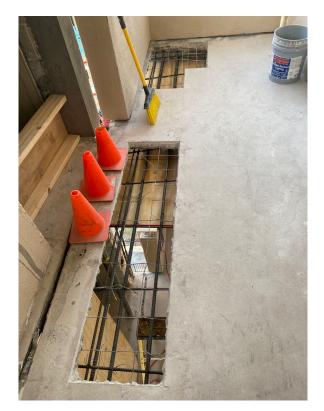

Picture 2: 6th floor walkway repair
