FIELD OVSERVATION REPORT PERMIT # BLDC-000287-2020

		Report No. 55	Page 1 of 1
Project:	Southpoint Condominium	Inspection For:	Restoration Project
Day/Date:	Monday, November 9, 2020	Job No.	19-1086
Location:	4453 S. Atlantic Ave, Ponce Inlet	Engineer:	Timothy J. Snook, P.E.
Contractor:	ACE Enterprises, LLC	Project Foreman:	Wes Swaim
Subcontractor:	N/A	Inspector:	Timothy J. Snook, P.E.
Weather:	80 Degrees @ 8:00 A.M. Overcast	Windy Rainy	
Workforce Total:	0		
Activities:	Concrete Inspection		

Observation Report:


Due to the windy and rainy weather, the Contractor will not be working today.

The Engineer was on-site to inspect the full depth concrete repair at Unit 108 (See Photo 1). The excavations has been formed. The excavation conformed to ICRI standards. The supplemental reinforcing steel was installed as directed. The top longitudinal #4 bars will be wet set during concrete placement. The excavation was approved to be cast.


UNITED ENGINEERING CONSULTANTS

I have Innove

Timothy J. Snook, P.E. Florida License No. 83208



This item has been electronically signed and sealed by Timothy J. Snook using a Digital Signature and date. Printed Copies of this Document are not considered signed and sealed and the SHA authentication code must be verified on any electronic copies.

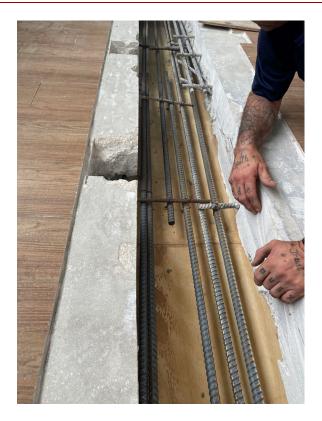

Picture 1: Excavation at Unit 108
