TED ENGINEERING CONSULTANTS, INC

Building Condition Surveys
Contract Administration
Corrosion Control Design
Structural Inspection & Design
Project Planning & Management

FIELD OVSERVATION REPORT PERMIT # BLDC-000287-2020

		Report No. 2	Page 1 of 1
Project:	Southpoint Condominium	Inspection For:	Restoration Project
Day/Date:	Friday, May 8, 2020	Job No.	19-1086
Location:	4453 S. Atlantic Ave, Ponce Inlet	Engineer:	Timothy J. Snook, P.E.
Contractor:	ACE Enterprises, LLC	Project Foreman:	Wes Swaim
Subcontractor:	N/A	Inspector:	Timothy J. Snook, P.E.
Weather:	60 Degrees @ 10:15 A.M. Sunny	Light Breeze 09	% Chance of Rain
Workforce Total:	4		
Activities:	Protect SGDs and rails, continue mobilization		


Observation Report:

Mobilization continues with setting up the rigging for swing stages.

The topside of the parking deck has had a majority of the coating removed (See Photo 1). GAR will waterblast the deck to remove any existing coating and to provide a surface profile for the new coating system. After the deck has been water blasted, the Engineer will sound the deck for concrete damage.

Protection for the sliding glass doors and guardrails on the 11 stack balconies is being installed. Protection of the guardrails on the walkways is in-progress (See Photo 2).


It was verified with the Property Manager that the existing window shutters on the 10/11 stack windows will be removed and disposed of.



4240 South Ridgewood Avenue, Suite 4, Port Orange, FL 32127 • (386) 256-7684 • office@unitedengineeringconsultants.com Certificate of Authorization No. 6607



Picture 1: Topside of the parking deck

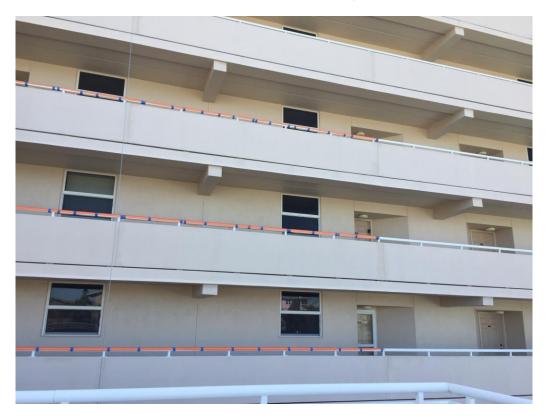

Picture 2: In-progress protection of the walkway guardrails



Picture 3: Swing stage mobilized on the 11 stack balconies
